





Clayton County 2024 Q2 Update

May 14, 2024 Collie Greenwood General Manager/CEO

Agenda

Operations Updates

MARTA 2040 Capital Expansion

Other News




Operations Updates



Mobility and Streetcar Ridership


RIDERSHIP

MARTA Monthly Ridership by Mode July 2019 - March 2024

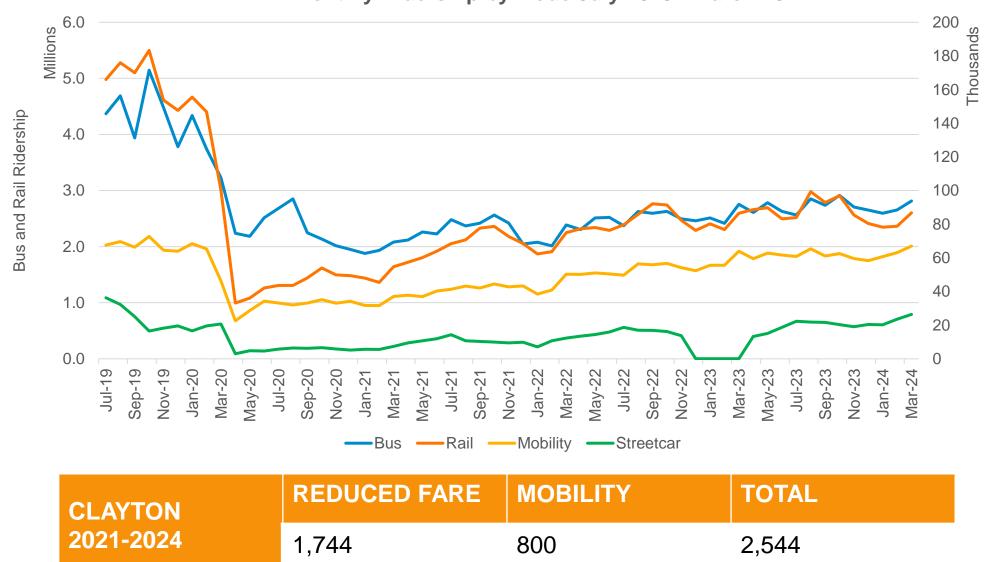


marta 📏

CLAYTON ROUTES

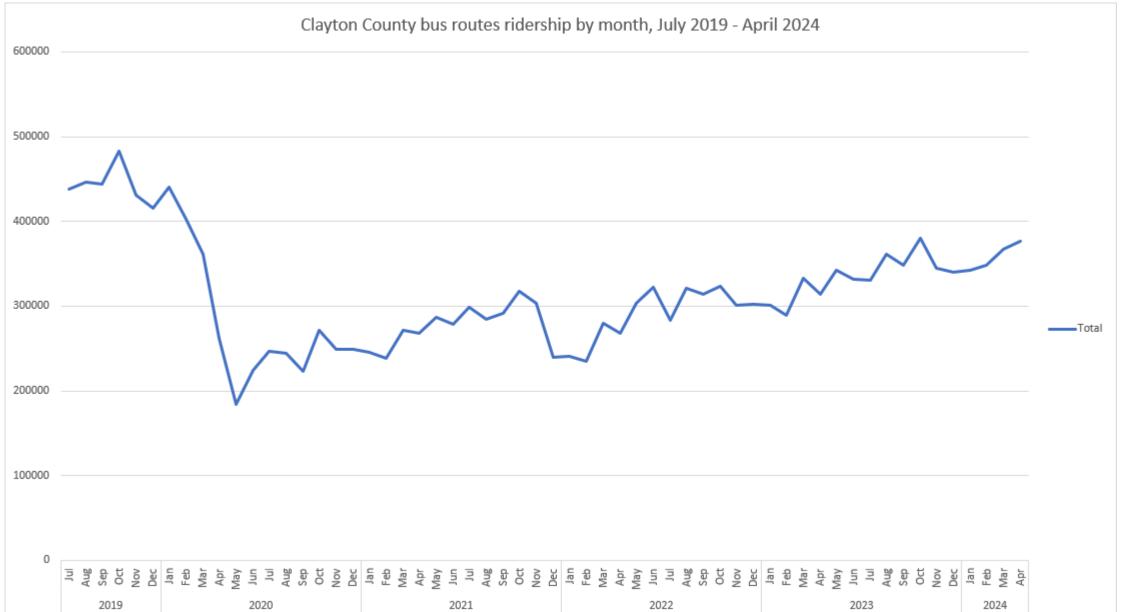



MARTA Monthly Mobility July 2019 - March 2024

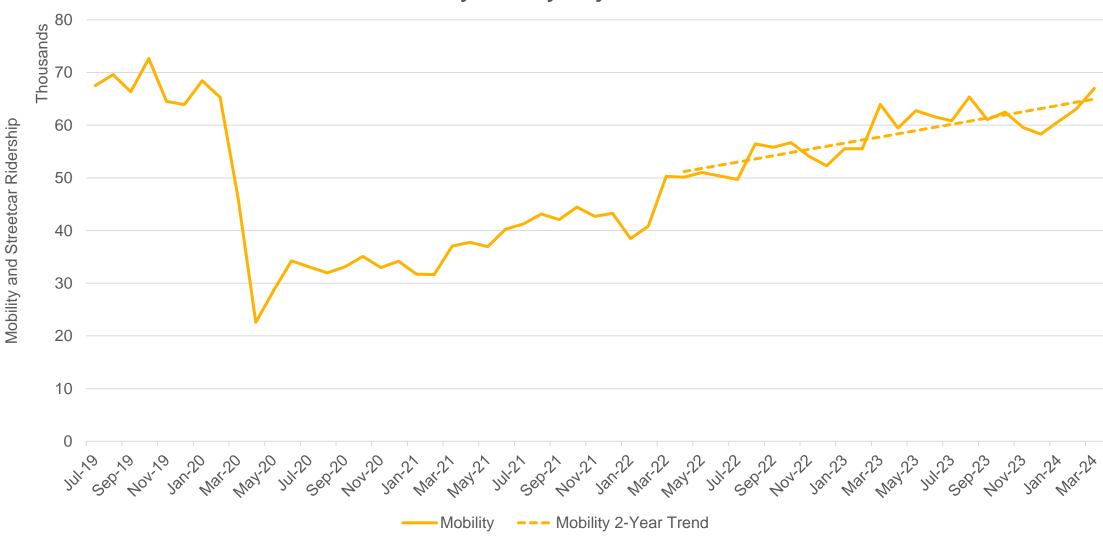




PROGRAM HIGHLIGHTS

	FY20	FY21	FY22	FY23	FY24
Amenities Delivery Pre-COVID Estimate	30 amenities per year				
Amenities Delivered	29	9	25	20	53 of 67
TOTAL					150

MARTA is making progress on the remaining 67 amenities for FY24:

FY24 Amenities Status

- √ 53 installed
- ✓ 5 under construction
- √ 7 in permitting
- ✓ 2 in design

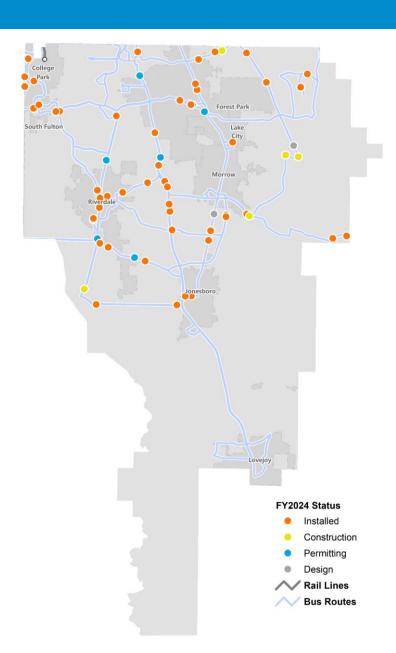



BUS STOP AMENITIES

212080 – Forest Pkwy & Phillips Dr







Serves:

Medical facilities, businesses, and residences

Routes:

193 – Morrow/Jonesboro

195 – Forest Parkway




This program will improve pedestrian conditions near high ridership bus stops and is currently in the planning phase.

- mix of high visibility crosswalks,
- ✓ curb extensions,
- ✓ medians and refuge islands,
- ✓ rapid-flash & pedestrian beacons

15 potential Safe Routes to Transit site concepts were shared with Clayton County staff for review and comments.



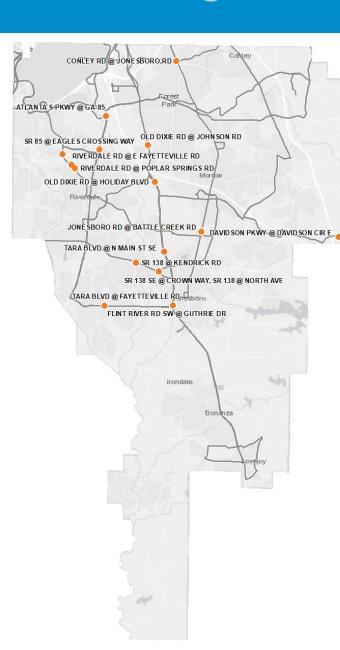

^{**}Sites shown are in preliminary planning and are subject to change based on potential NEPA, final design and permitting constraints.



AIRPORT STATION REHAB



Investment: \$55M

Projected Completion: June 2026







MARTA 2040 Capital Expansion



JUSTICE CENTER TRANSIT HUB UPDATE

Project Status:

- ✓ Final design on track for completion in Summer 2024
- ✓ Fencing between the transit hub and the Justice Center design is complete with help from county staff
- Procurement coming soon for expedited installation

Investment: \$21.5M

Projected Completion: December 2026







MULTI-PURPOSE OPERATIONS & MAINTENANCE FACILITY UPDATE

Project Status:

- Demolition bid package just released
- ✓ 90% Plans for new facility are complete
- √ 100% Plans will be completed Q4 2024



Investment: \$285M

Projected Completion: August 2029




MARTA RAPID SOUTHLAKE (BRT) UPDATE

- Amended LPA resolution approved by the Board of Commission
- Final designer solicitation underway
- ✓ Submit updated NEPA checklist and environmental special studies
- Class of Action determined by FTA
- ✓ Submission of FTA CIG Small Starts application in Summer 2024
- Projected Service Start: 2030*

Investment: \$390M

Projected Revenue Service: 2030

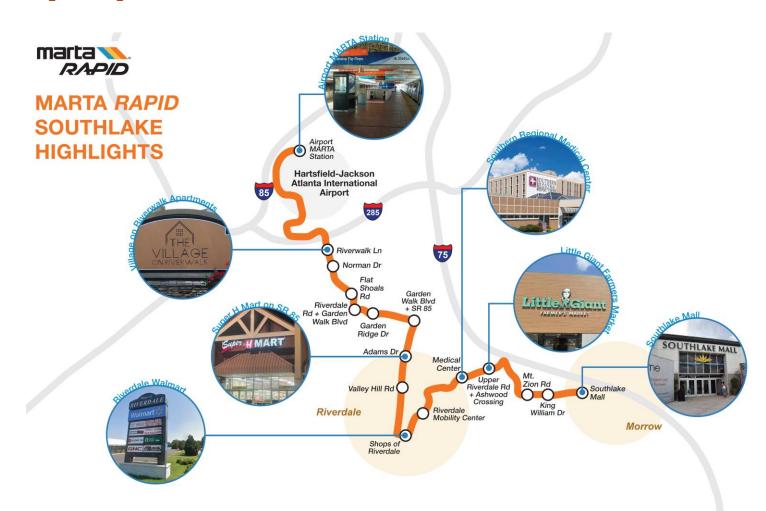



Public Open House March 28, 2024 – Southern Regional Medical Center – Education Center





Other News



MARTA FY2025 BUDGET HEARINGS

- ✓ Wed. May 15, DeKalb (Maloof Auditorium) 7PM
- Thur. May 16, Fulton-City of Atlanta (MARTA HQ) 7 PM
- Thur. May 23, Board Presentation of Resolution to adopt the Proposed FY2025 Budgets
- ✓ Thur. June 13, Board Adoption of FY2024 Budgets





Top Projects
by FY2025
Budget
Clayton County
(\$M)

Project Description	FY25 Budget
MARTA Rapid Southlake	11.5
Justice Center Transit Hub	6.6
Multipurpose O&M Facility – Clayton Share	5.0
SR 54 High-Capacity Transit (BRT)	4.7
Total	27.8



STAKEHOLDER MEETINGS

Citizen Advisory Board (4/17)

Quarterly meeting held with positive feedback on TOD opportunities around BRT

Clayton State University (4/19)

- ✓ Open communication for projects
- Explore partnerships for events and recruiting
- ✓ Create a pipeline for workforce development





COMMUNITY ENGAGEMENT







Thank You

